


## Foothill High School

Project No.	Funding	Project	Schedule	Project Cost
1	G	Quad	Complete	\$ 5.9 m
2	G	<b>Science Center</b> Under Construction Includes Tennis Court Resurfacing (Complete)	Now - Dec. 09	\$ 19 m
3	G/L	<b>Aquatics Center</b> Demolition - Complete Construction Portion - In DSA Completion	Sep. 10	\$ 3.6 m
4	L	<b>Math Remodel</b> Design DSA Bid Const.	Aug.- Oct. 09 Nov. - Mar. 10 Apr. 10 - May 10 June 10 - Sept. 10	\$ 3.1 m
5	L	<b>New Gym/ Multi-Purpose</b> Design DSA Bid Const.	Aug. - Nov. 09 Dec. 09 - May 10 June - July 10 Aug. 10 - July 11	\$ 6.1 m
6	L	<b>Site work</b> Design DSA Bid Const.	Aug.- Oct. 09 Nov. - Mar. 10 Apr. 10 - May 10 June 10 - Sept. 10	\$ 3 m
7	L	<b>Locker Rooms Remodel</b> Design DSA Bid Const.	Aug.- Oct. 09 Nov. - Mar. 10 Apr. 10 - May 10 June 10 - Sept. 10	\$ 1.5 m

# Foothill High School

## Foothill High School – Site Plan - Proposed Work

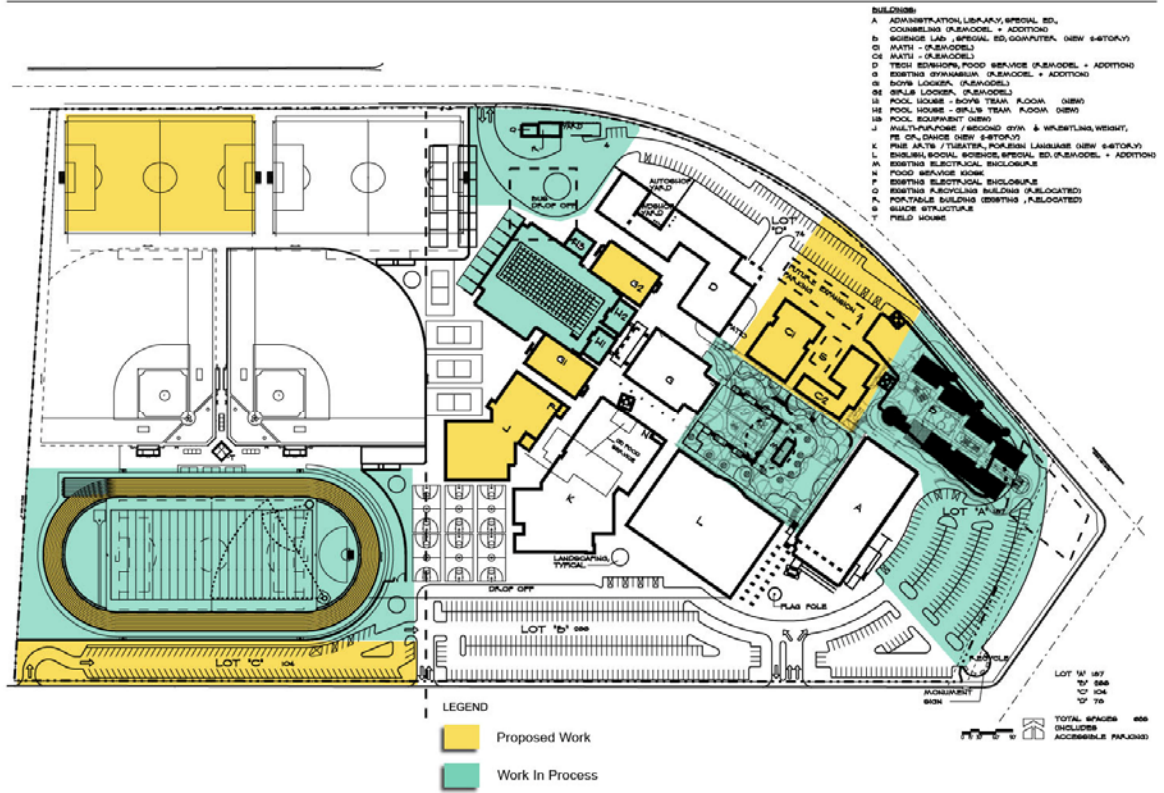

## Foothill High School – Pool



Foothill High School – Quad



Foothill High School – Science Center

